


Pre-Commissioning Tasks

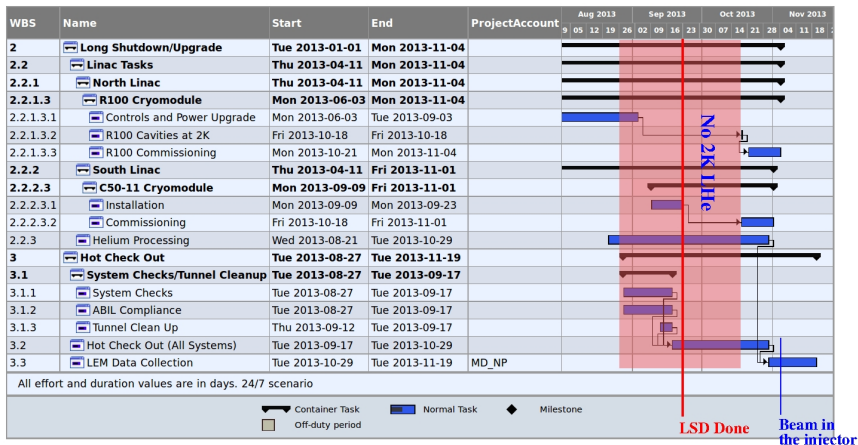

- At present it all fits, but.

But....

- At present it all fits, **but**.
- Very concerned about the stacked up leading up to Beam Operations.
 - ▶ Final weeks of HCO also include commissioning of R100 and C50-11.
 - ▶ Will this pass muster at the Director's Commissioning Review?
- Can we reduce the number of concurrent activities during HCO?
 - ▶ Don't need to remind people about the YR incident, do I?
- Is there enough time for He processing?
- Can the no LHe@2K period be reduced?

Other Commissioning News

- First meeting of the Commissioning Advisory Board is this afternoon.
 - ▶ Fulvia is the chair
 - ▶ This meeting is an organizational one, plus an extremely dry run (with olives?) of the presentations for the Director's Commissioning Review.
- Director's Commissioning Review scheduled for June 6 and 7.
 - ▶ One day of talks and a tunnel tour.
 - ▶ Close-out after lunch on the 7th.
- June starts the weekly occurrence of System Readiness reviews
 - ▶ Readiness orientation is on Wed May 29th after the 8am meeting in Bldg 87 (aka the MCC startup building).
