



ID	Task Mode	Task Name	Work	Duration	Start	Finish	Predecessor
1		Hall D Operations Resumption	330.88 hrs	26 days	Mon 6/8/20	Tue 7/14/20	
2		Open Hall D for Recovery Procedures	1.6 hrs	0.1 days	Mon 6/8/20	Mon 6/8/20	
3		Administration procedures & discussion	32 hrs	2 days	Mon 6/8/20	Wed 6/10/20	2
4		Detectors (Reference Checklists)	77.76 hrs	15.9 days	Wed 6/10/20	Wed 7/1/20	
5		Stevens -Oversite Supervision	38 hrs	13.9 days	Wed 6/10/20	Mon 6/29/20	
6		Prework walkdown & checklist	1 hr	0.13 days	Wed 6/10/20	Mon 6/15/20	3
7		Turn on Microscope fan	0.8 hrs	0.1 days	Wed 6/10/20	Wed 6/10/20	3
8		Turn on CDC Blowers	0.8 hrs	0.1 days	Wed 6/10/20	Wed 6/10/20	7
9		Adjust BCal N2 purge	0.8 hrs	0.1 days	Wed 6/10/20	Wed 6/10/20	8
10		ComCal N2 Purge	0.8 hrs	0.1 days	Wed 6/10/20	Wed 6/10/20	9
11		ComCal - Reactivate Chiller	4 hrs	0.5 days	Wed 6/10/20	Wed 6/10/20	10
12		Bcal Chiller US - Use Procedures	6.4 hrs	0.8 days	Thu 6/11/20	Thu 6/11/20	11
13		Prework walkdown & checklist	1 hr	0.13 days	Thu 6/11/20	Mon 6/15/20	12
14		Bcal Chiller DS - Use Procedures	6.4 hrs	0.8 days	Thu 6/11/20	Fri 6/12/20	12
15		FDC Chillers - Use Procedures	4 hrs	0.5 days	Fri 6/12/20	Mon 6/15/20	14
16		Re-establish Detectors Gas Supply	12 hrs	1.5 days	Wed 6/10/20	Mon 6/29/20	8
17		DIRC	39.76 hrs	12.9 days	Mon 6/15/20	Wed 7/1/20	
18		Spiegel - Oversight Supervision	39.76 hrs	12.9 days	Mon 6/15/20	Wed 7/1/20	15
19		Users Group Checklists	16 hrs	2 days	Tue 6/30/20	Wed 7/1/20	5
20		Prework walkdown & checklist	1 hr	0.06 days	Mon 6/15/20	Mon 6/15/20	
21		Readjust N2 purge	0.8 hrs	0.1 days	Mon 6/15/20	Mon 6/15/20	21
22		Restart Water Cart	1.04 hrs	0.13 days	Mon 6/15/20	Mon 6/15/20	
23		Add water when necessary	0 hrs	0.1 days	Mon 6/15/20	Mon 6/15/20	
24		Refill Both Optical Boxes	16 hrs	2 days	Mon 6/15/20	Wed 6/17/20	22
25		Prework walkdown & checklist	1 hr	0.06 days	Wed 6/17/20	Wed 6/17/20	24
26		Replace Water filters & UV Lamp	1.04 hrs	0.13 days	Wed 6/17/20	Wed 6/17/20	24
27		Obtain Water Samples	1.04 hrs	0.13 days	Wed 6/17/20	Wed 6/17/20	26
28		Secure release by RADCON	1.04 hrs	0.13 days	Wed 6/17/20	Wed 6/17/20	27
29		Turn on Tagger NMR Probe	0.8 hrs	0.1 days	Mon 6/15/20	Mon 6/15/20	
30		Vacuum Systems	18.08 hrs	2 days	Wed 6/17/20	Fri 6/19/20	
31		Spiegel - Oversight Supervision	18.08 hrs	2 days	Wed 6/17/20	Fri 6/19/20	
32		Verify Goni. Valves Operation w/	2 hrs	0.25 days	Wed 6/17/20	Wed 6/17/20	28
33		Verify Tagger Valve Operation w/	2 hrs	0.25 days	Wed 6/17/20	Thu 6/18/20	32
34		Prework walkdown & checklist	1.04 hrs	0.13 days	Thu 6/18/20	Fri 6/19/20	33
35		Verify 10" Beam Pipe Tag/Coll. Cave Valve Operation w/ MCC	2 hrs	0.25 days	Thu 6/18/20	Thu 6/18/20	33
36		Turn on Collimator Cave Vacuum Pumps w/ Procedure	4 hrs	0.5 days	Thu 6/18/20	Thu 6/18/20	35

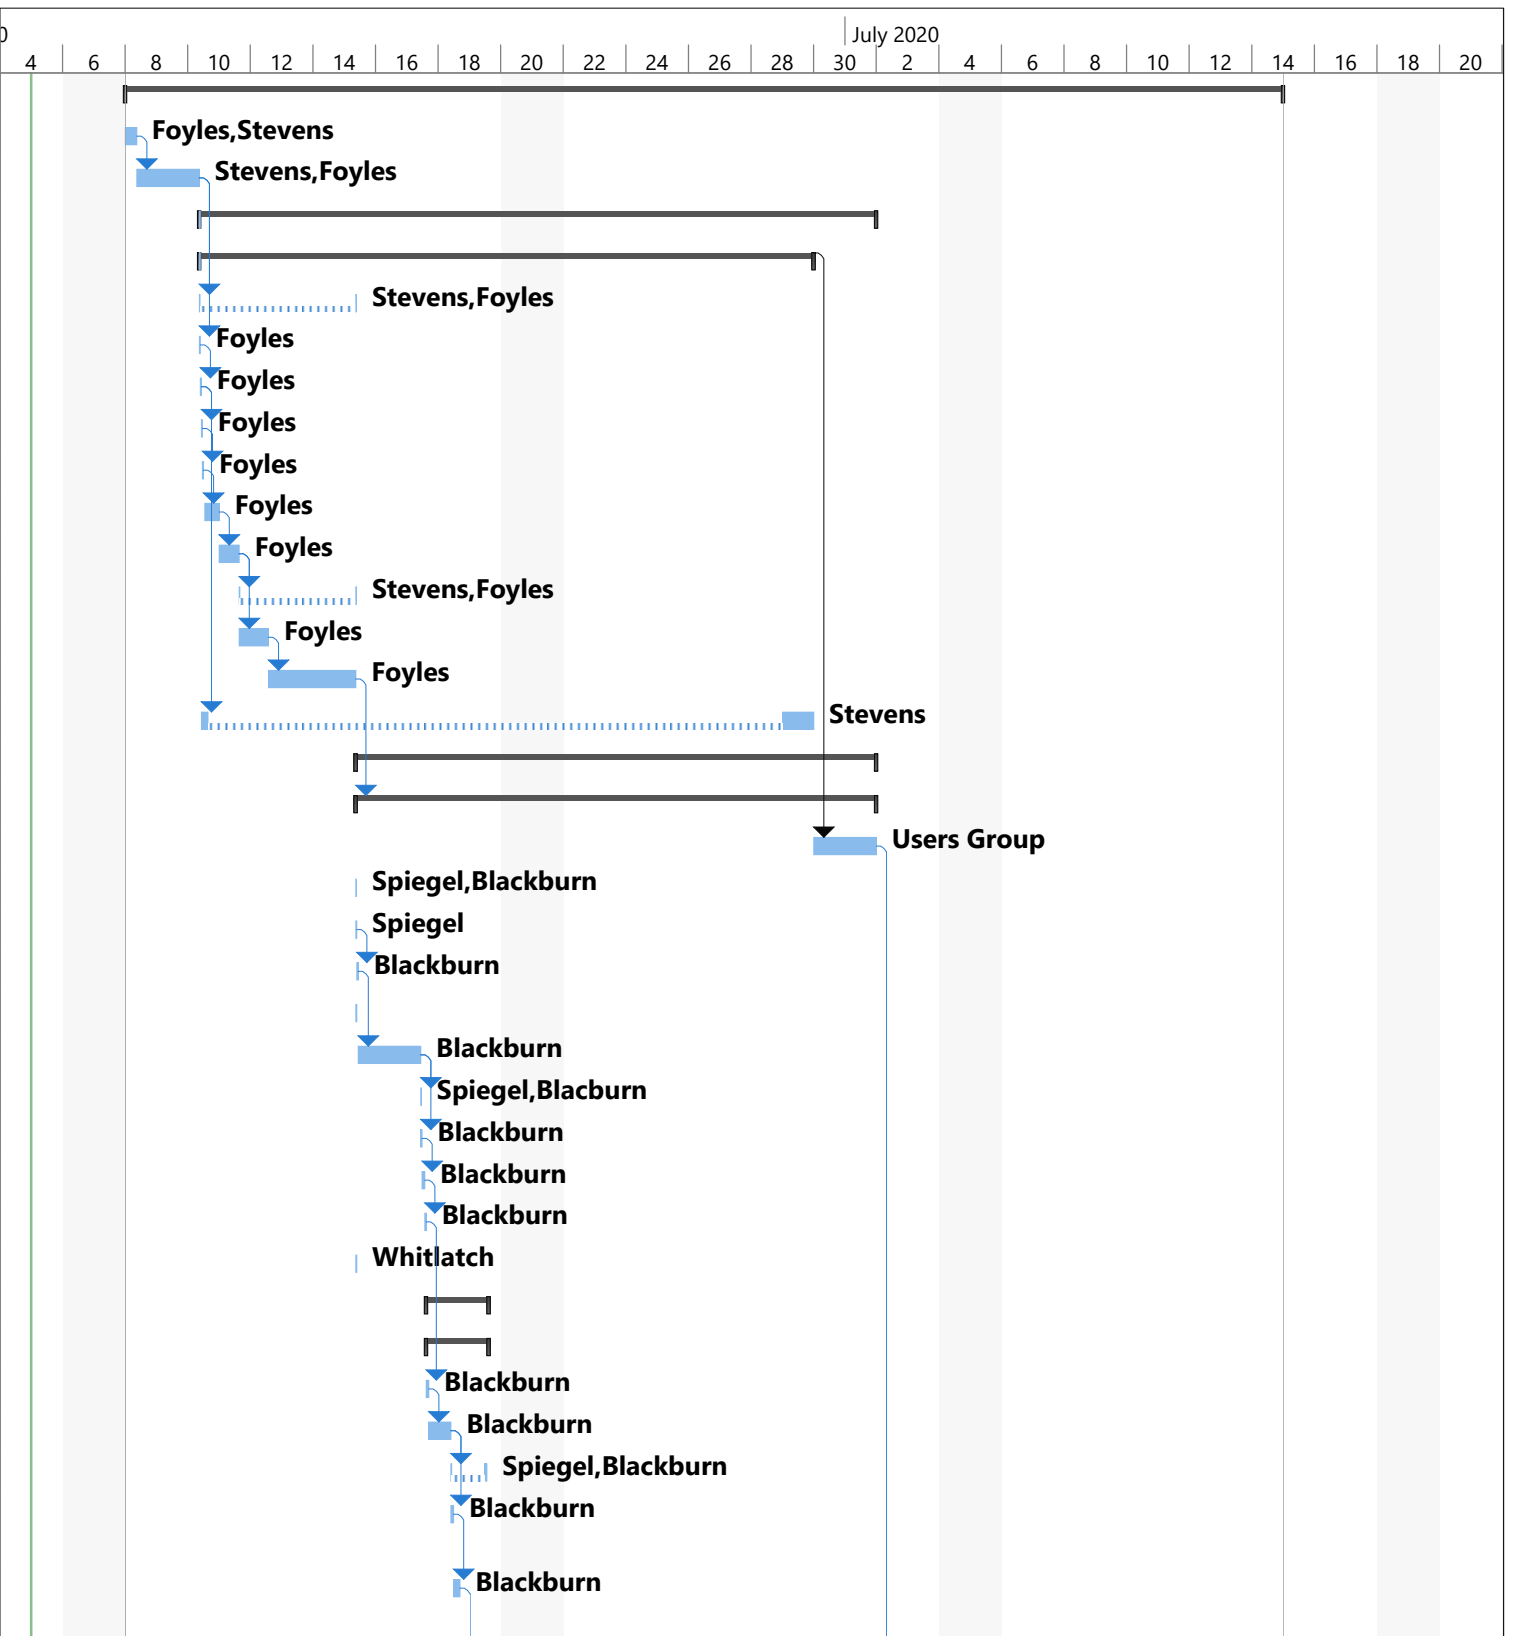

Project: Project Hall D Resumpt
Date: Fri 6/5/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

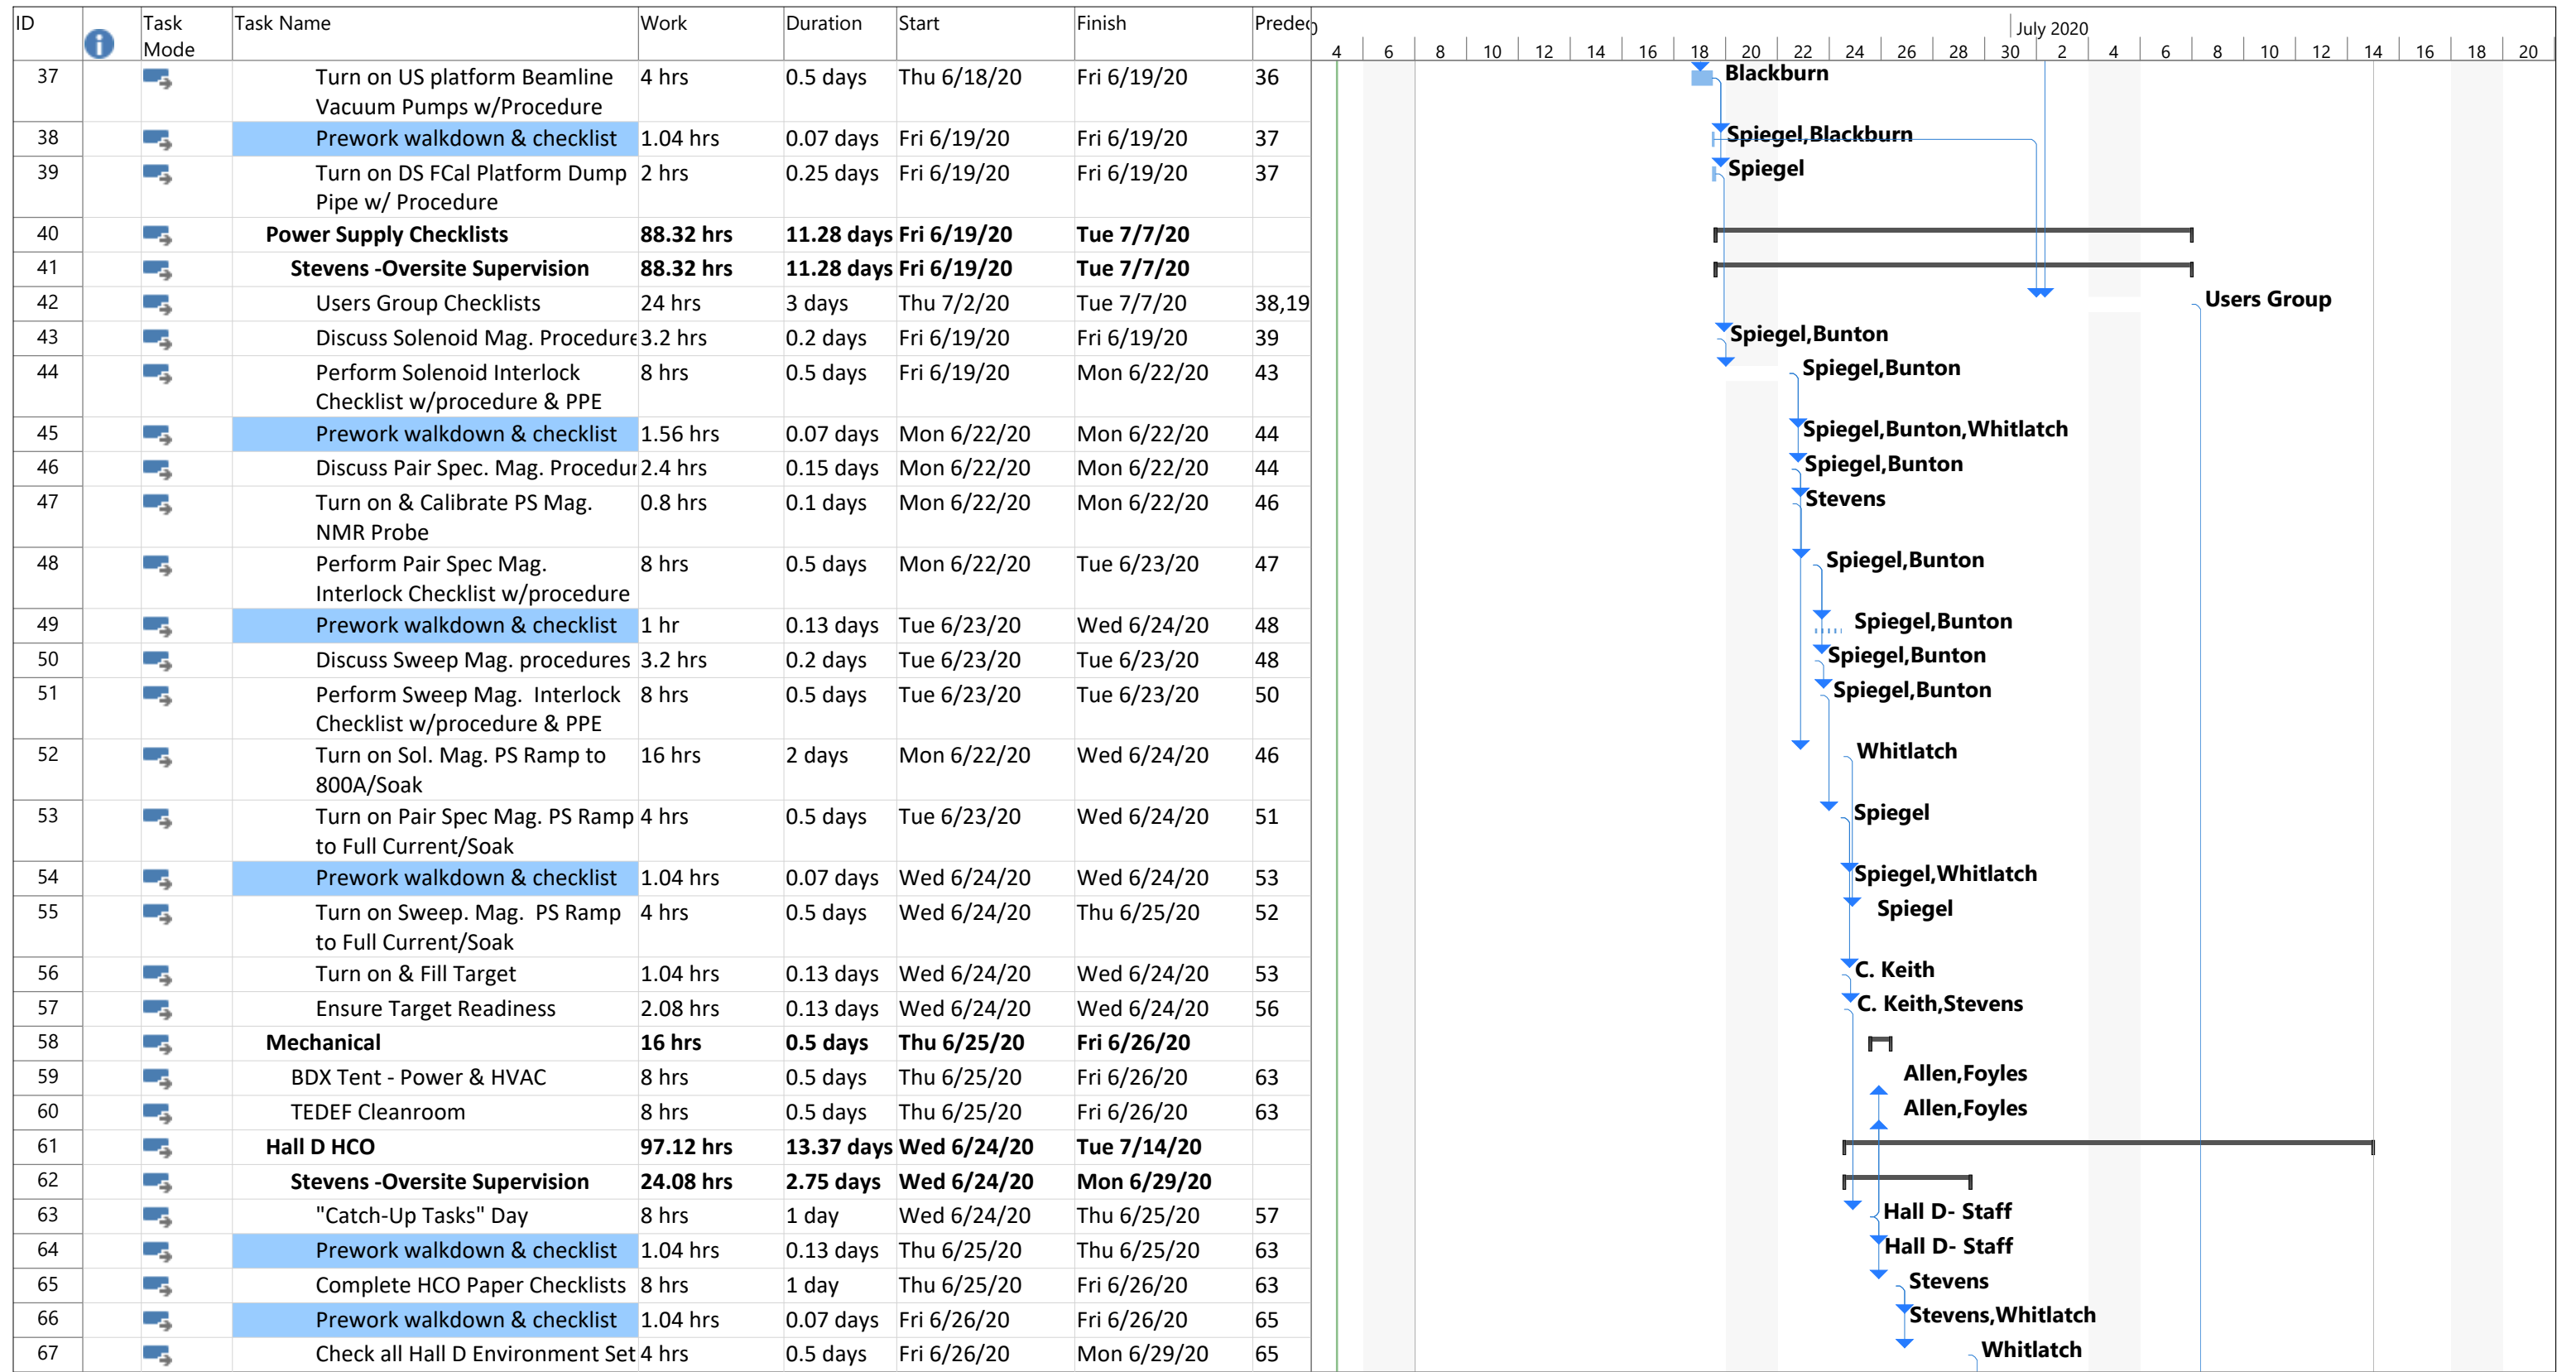

Project: Project Hall D Resumpt
Date: Fri 6/5/20

Task	Project Summary		Manual Task		Start-only	[Deadline	↓
Split	Inactive Task	Duration-only		Finish-only]	Progress	
Milestone	Inactive Milestone	◆	Manual Summary Rollup		External Tasks		Manual Progress	
Summary	Inactive Summary	▬	Manual Summary		External Milestone	◆		

ID	Task Mode	Task Name	Work	Duration	Start	Finish	Predecessor	July 2020																											
68		Turn on, Verify & Start PXI data	2 hrs	0.25 days	Mon 6/29/20	Mon 6/29/20	67																												
69		Electrical - Beam Run Equipment	73.04 hrs	10.62 days	Mon 6/29/20	Tue 7/14/20																													
70		Prework walkdown & checklist	1.04 hrs	0.13 days	Mon 6/29/20	Mon 6/29/20	68																												
71		Complete HCO "Mechanical" Checklists	32 hrs	2 days	Mon 6/29/20	Wed 7/1/20	68																												
72		Users Group Checklists	40 hrs	5 days	Wed 7/8/20	Tue 7/14/20	42,71																												
73		Prepare Hall D for Beam	8 hrs	1 day	Mon 6/29/20	Tue 6/30/20	68																												

Project: Project Hall D Resumpt
Date: Fri 6/5/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
