
Gestation






APF Short Institution

Commissioning Update

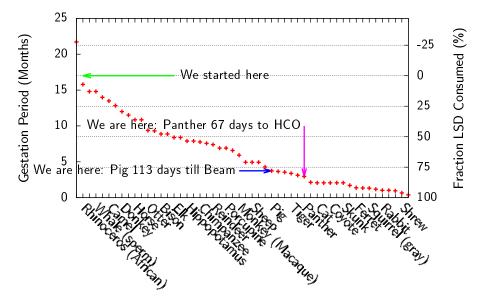

Jefferson Lab

Path to Beam & Accelerator Readiness Reviews



- R1: Consider rescheduling the ARR to a time when a majority of the hardware and software has been hot checked and the operators have been trained.
- R2: Consider increasing the ARR Team membership with the appropriate experts.



APF Short Institution

Commissioning Update





✓Facilities LCW, Cooling Towers, Power Distribution, Chilled Water, Fire Protection.

✓ Cryogenics CHL-1, CHL-2, HDR and ESR refrigerators

Safety Systems PSS, MPS, BELS, Beam Containment, Shielding

Chair Steve Suhring Date 2013-07-11

Software Controls, High Level Applications, System Administration, Networking and Cyber security.

Chair Matt Bickley Date 2013-07-18

Transport Magnets, Magnet Power Systems, Vacuum and Alignment

Chair Matt Bickley Date 2013-07-25





Diagnostics, Instrumentation and Controls Beam Position Monitors, Viewers, Harps, Vacuum monitoring, Beam Imaging, Beam Current Monitors, etc. Chair Matt Bickley

Date 2013-08-01

Acceleration SRF, LLRF controls, RF Power and Master Oscillator signal and distribution

Chair Steve Suhring Date 2013-08-08

RADCON Shielding, Beam Containment

Chair Steve Suhring Date TBD



APF Short Institution

Commissioning Update



