

DSG-Hall A ECAL Weekly Meeting


Date: March 14, 2024

Time: 09:00 – 10:00

Attendees: Deb Biwas, Jimmy Caylor, Donald Jones, Simona Malice, Marc McMullen, Albert Shahinyan, and Bogdan Wojtsekhowski

1. Six-supermodule test stand

1. Don has shut down the test stand prior to a planned power outage and will change out the power supply output connectors to connectors supplied by Marc that work with the new power supply interface chassis
2. Marc has verified that the test stand crystal and control temperatures are being archived using EPICS
 - Plots available via myaPlot
3. Marc has developed a wiring diagram for the power supply interface chassis, which will be fabricated by Mindy Leffel
 - Power supply interface chassis number one is 75% complete

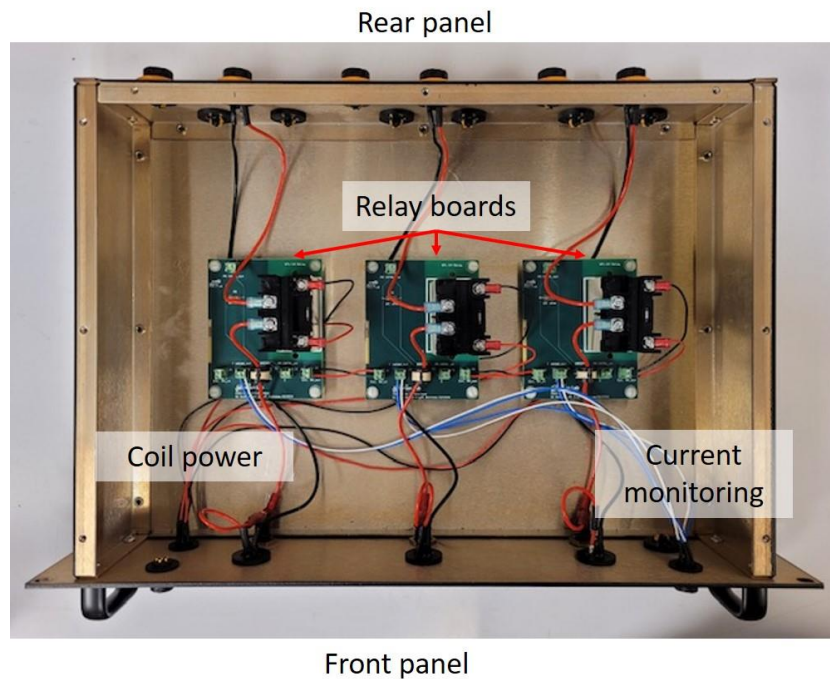

2. Full system installation

1. 20 supermodules have been tested with the mu-metal + PMT
 - 3 supermodules are ready for testing during G-nrp in mid-April
 - 46 mu-metal shields are ready for installation
2. 480 high voltage cables have been fabricated and are located in the Engineering Services building
