

DSG Moller

Date: 07/05/2023

Time: 11:00 – 12:00

Attendees: Peter Bonneau, Aaron Brown, Pablo Campero, Brian Eng, Kaiyi Hall, and Marc McMullen

1. OCEM MPS Remote Interface

Brian Eng

1. Draft version of [remote command reference](#) received; requested details on factory testing as well as final version
 - Still no details on interlock connector

2. Voltage Comparators


Probir Ghoshal, Brian Eng

1. Specifications submitted to [document control](#)
 - Will be used to submit to vendors for bid
 - Depending on cost and/or lead time, might need to develop in-house

3. Flowmeters

Brian Eng, Kaiyi Hall



1. Received two flowmeters ([instruction manual](#)) —one connected to Siemens PLC the other for Kaiyi to start integration into prototype test stand
 - Analog output for temperature verified, as well as relay outputs with DMM; no flow available

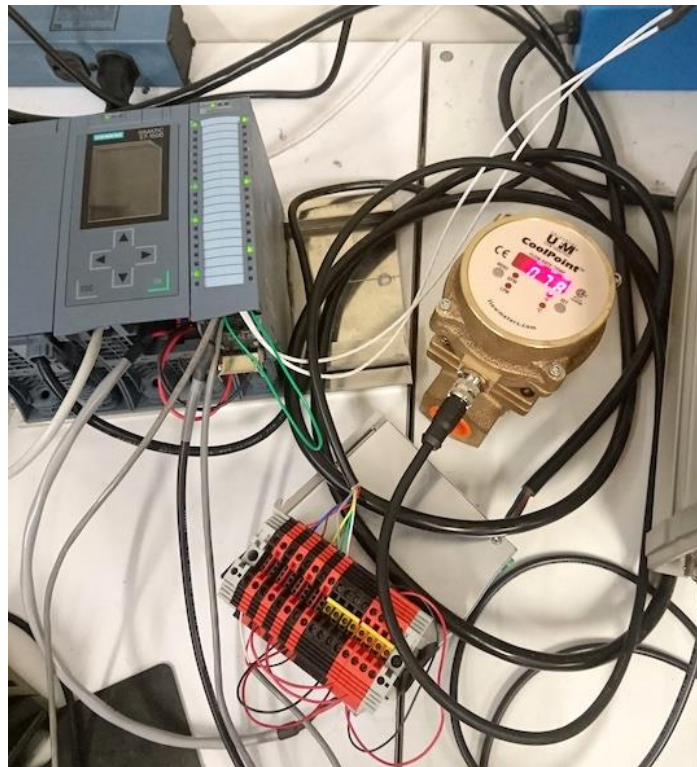

4. Siemens Software Licensing

Brian Eng

1. Evaluation period for STEP 7 software expired, so license from online software portal was installed locally on computer; fails to get a license. Support ticket filed with Siemens.
 - Can open project files and edit some things (PLC modules, tags), but cannot edit code

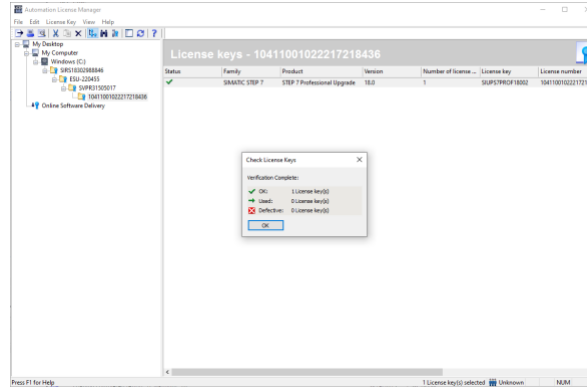

5. Voltage Tap Drawing

Kaiyi Hall

1. Starting on Torus Magnet 4
