

12GeV LSD Existing Plan

CHL ON 'till August


FEL ON

Power Permit

Cryomodule
Commissioning

Two S/R 's for rework

ATLis Work Map

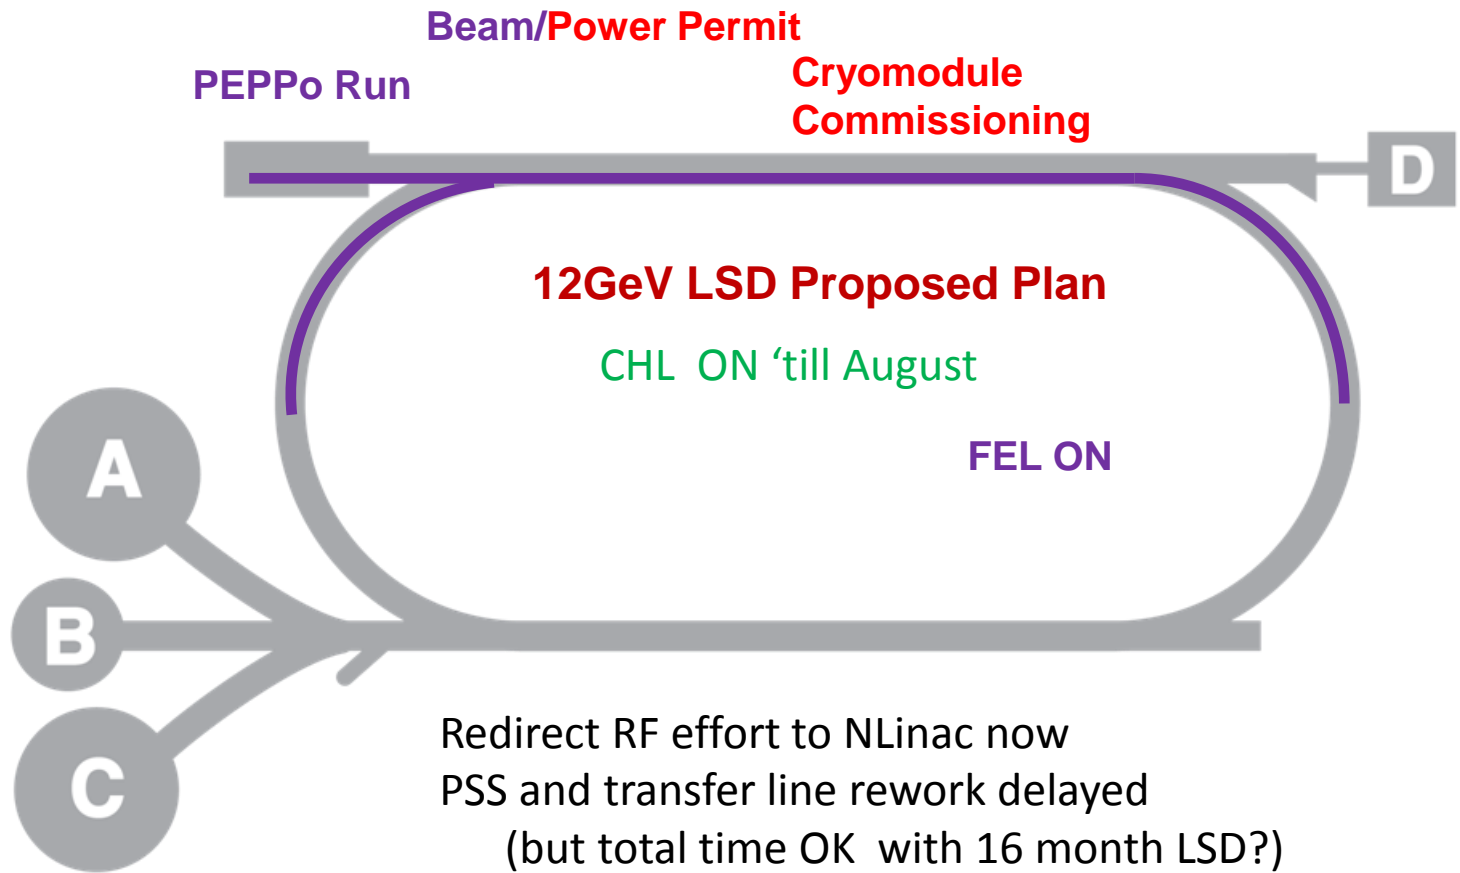

Beam/Power Permit

PEPPo Run

**Cryomodule
Commissioning**

12GeV LSD Proposed Plan

CHL ON 'till August

FEL ON



Redirect RF effort to NLinac now
PSS and transfer line rework delayed
(but total time OK with 16 month LSD?)

Cryomodule Commissioning has 'right of way'
PEPPo able to run
Three S/R 's for rework

No change to FEL running

**ATLis Work Map
12GeV LSD Proposal**
