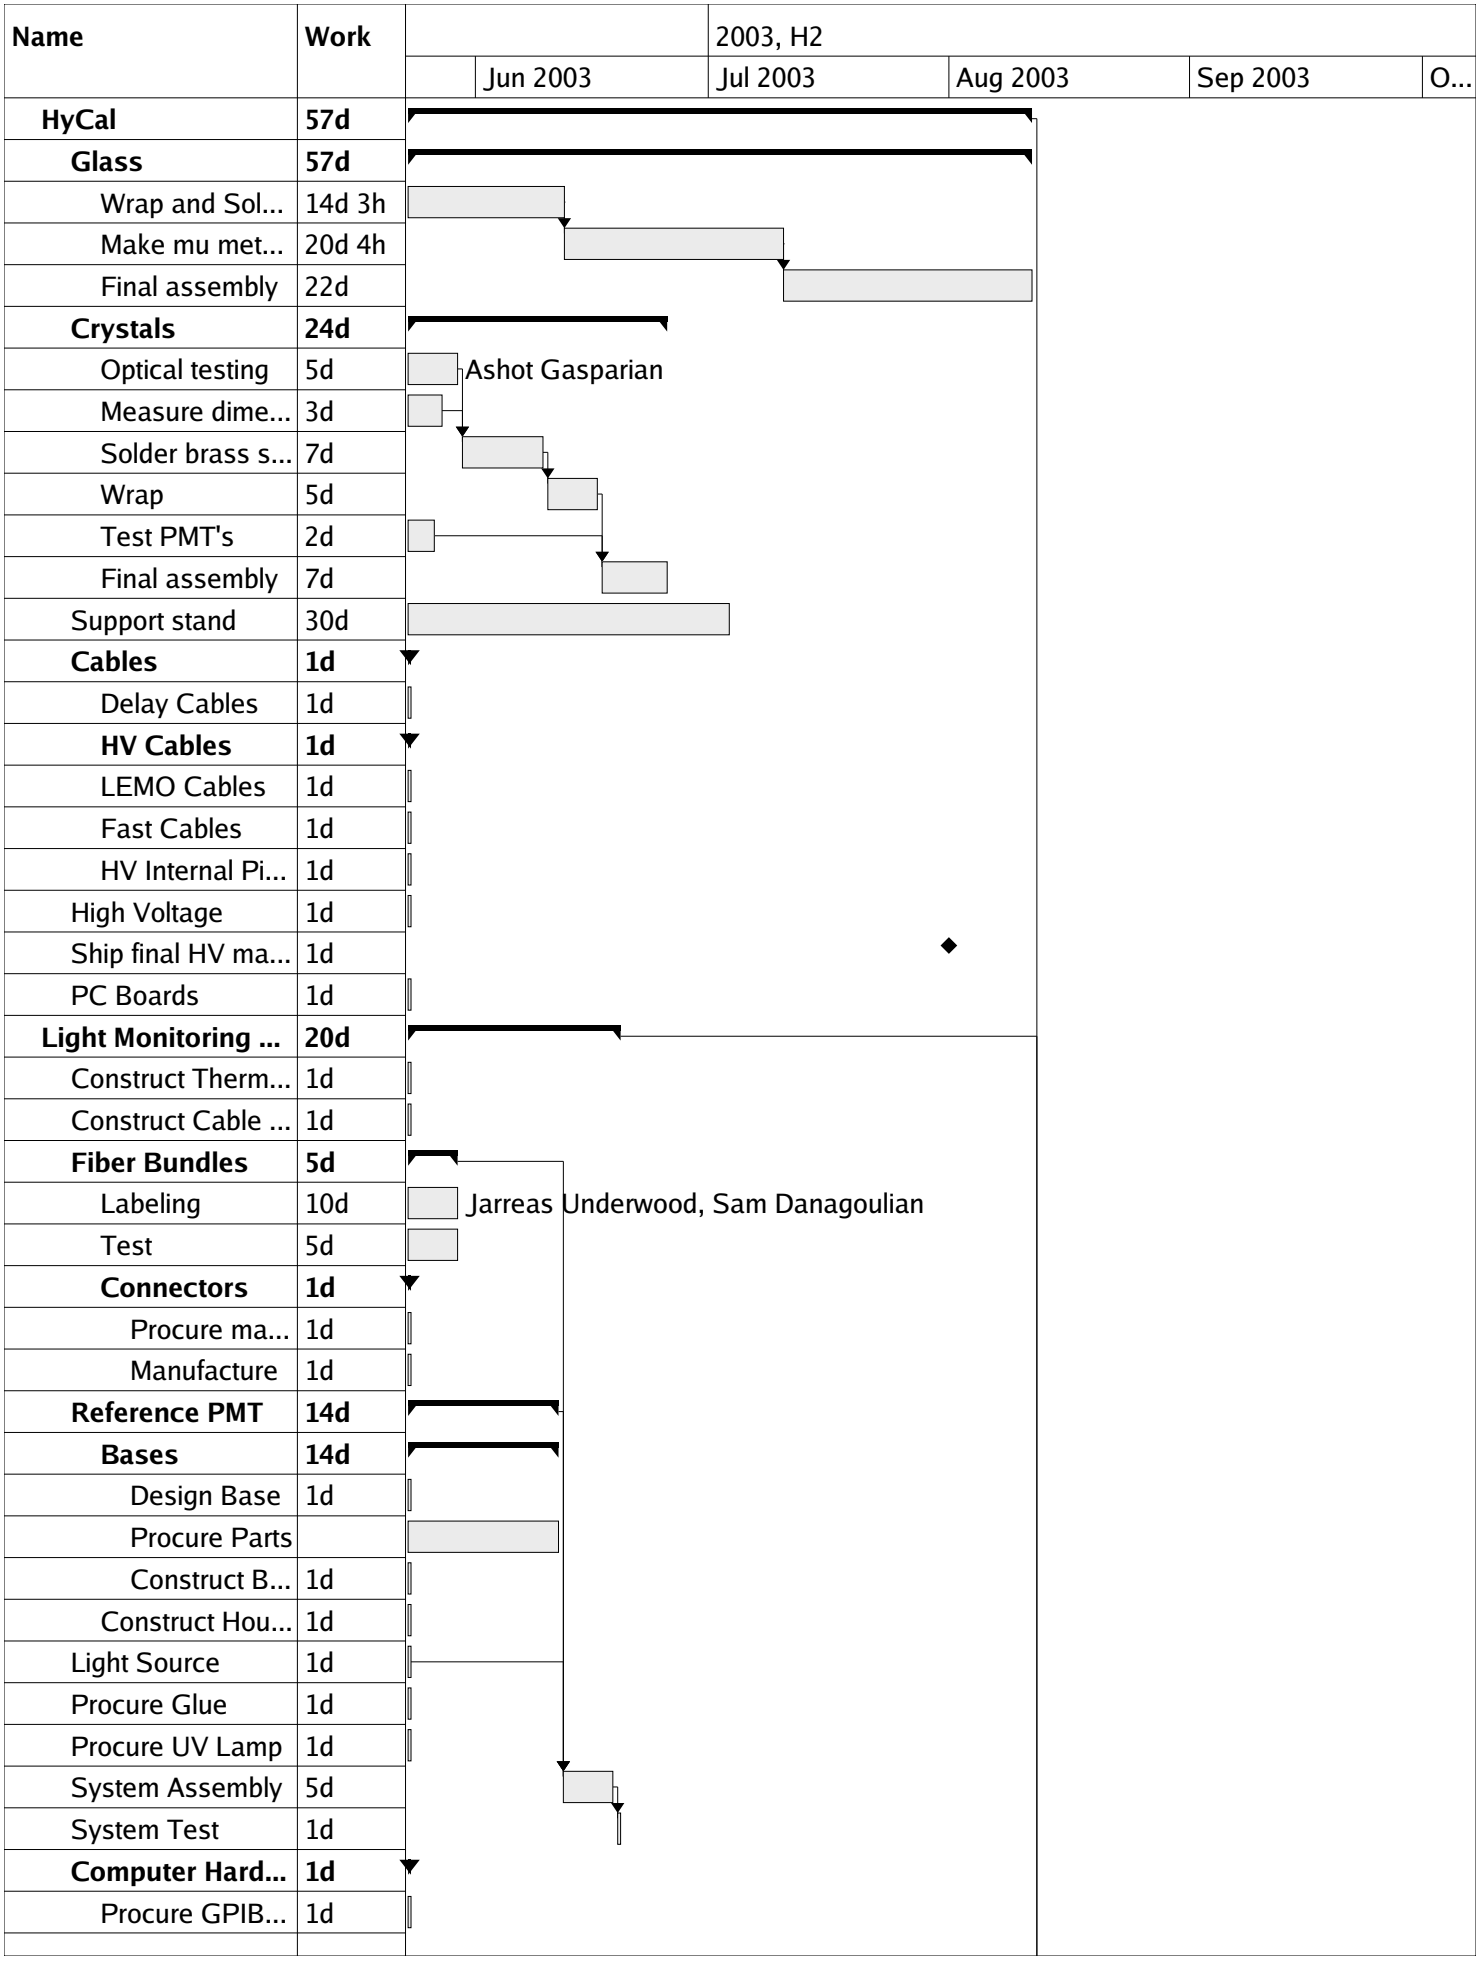
Name
Work
2003, H2
Jun 2003
Jul 2003
Aug 2003
Sep 2003
O...
HyCal 57d
Glass 57d
Wrap and Sol... 14d 3h
Make mu met... 20d 4h
Final assembly 22d
Crystals 24d
Optical testing 5d
Ashot Gasparian
Measure dime... 3d
Solder brass s... 7d
Wrap 5d
Test PMT's 2d
Final assembly 7d
Support stand 30d
Cables 1d
Delay Cables 1d
HV Cables 1d
LEMO Cables 1d
Fast Cables 1d
HV Internal Pi... 1d
High Voltage 1d
Ship final HV ma... 1d
PC Boards 1d
Light Monitoring ... 20d
Construct Therm... 1d
Construct Cable ... 1d
Fiber Bundles 5d
Labeling 10d
Jarreas Underwood, Sam Danagoulian
Test 5d
Connectors 1d
Procure ma... 1d
Manufacture 1d
Reference PMT 14d
Bases 14d
Design Base 1d
Procure Parts
Construct B... 1d
Construct Hou... 1d
Light Source 1d
Procure Glue 1d
Procure UV Lamp 1d
System Assembly 5d
System Test 1d
Computer Hard... 1d
Procure GPIB... 1d

			2004, H1			
	Nov 2003	Dec 2003	Jan 2004	Feb 2004	Mar 2004	Apr 2...

			2004, H2			
	May 2004	Jun 2004	Jul 2004	Aug 2004	Sep 2004	Oct 2004

Control/Monitori...	1d
Veto Counters	30d
Assembly, Test Lab	41d
All hardware comp...	1d
Cosmic Ray Test	2d
Vacuum Box	1d
Total Absorption ...	**1d**
Placement Decis...	1d
Stand	**1d**
Hardware	1d
Motion Control	1d
Target Ladder	**1d**
Target Mapping	1d
Motion Control	1d
Pair Spectrometer	**1d**
Module Constru...	1d
Module Installation	1d
ADC Read-Out	1d
Extra HV Power ...	1d
Tagger	**3d**
Electronics	**3d**
Fabrication	1d
Installation	1d
Commission	1d
Hall Probe/NMR	**1d**
System Design	1d
Procurement	1d
Install	1d
Read-Out/Co...	1d
Dipole Magnet	**1d**
NMR	**1d**
Hardware Ch...	1d
Software Che...	1d
Beam Position Mo...	1d
Luminosity/Tagger ...	2d
Disassemble, Test ...	1d
Install, Hall B	22d
Commisioning Run	8d
Physics Run	35d
